PROJECT PLANNING PHASE

Product Backlog, Sprint Planning & Estimation

ServiceNow-Based Employee Laptop Request Application

Project Name	ServiceNow-Based Employee Laptop Request Application	**Planning Horizon**	4 short sprints (proposed)

1. Product Backlog and Sprint Schedule

Sprint 1	Request Submission	USN-1	As an employee, I can complete a laptop request form with the required details.	3	High	Project team
Sprint 1	Request Submission	USN-2	As an employee, I receive confirmation after my request is submitted.	2	High	Project team
Sprint 1	Request Validation	USN-3	The system checks mandatory fields and prevents incomplete submissions.	3	High	Project team
Sprint 1	Request Records	USN-4	The request is saved as a record with an automatically generated request number and initial status.	3	High	Project team
Sprint 2	Manager Approval	USN-5	The request is routed to the employee's manager, and the approval decision is recorded.	5	High	Project team
Sprint 2	Approver Communication	USN-6	The manager receives an email or clear notification path to review the request.	3	High	Project team
Sprint 3	Notifications	USN-7	The requester receives updates when submission and approval status change.	3	High	Project team
Sprint 3	Request Tracking	USN-8	The requester can check the current status of their laptop request.	3	High	Project team
Sprint 4	IT Administration	USN-9	An authorized IT administrator can review requests and approval outcomes.	3	Medium	Project team
Sprint 4	Testing & Refinement	USN-10	The team tests the end-to-end workflow, checks access and fixes issues.	5	High	Project team

Note: “Project team” is used because individual team-member names were not provided. Story-point estimates are provisional and should be reviewed by the team.

2. Project Tracker: Planned Sprint Schedule

Sprint	Total Story Points	Duration	Start	Planned End	Points Completed	Actual Release
Sprint 1	11	1 week	To be scheduled	To be scheduled	Not yet available	Not yet available
Sprint 2	8	1 week	To be scheduled	To be scheduled	Not yet available	Not yet available
Sprint 3	6	1 week	To be scheduled	To be scheduled	Not yet available	Not yet available
Sprint 4	8	1 week	To be scheduled	To be scheduled	Not yet available	Not yet available
Total	**33**	4 weeks	—	—	To be updated	—

3. Velocity

The template defines average velocity as story points completed per sprint, and also demonstrates an iteration-unit calculation using sprint duration. Since this is a proposed plan and no completed sprint data is available, actual team velocity cannot yet be measured.

Total planned points	11 + 8 + 6 + 8	33 points
Average planned workload	33 ÷ 4 sprints	8.25 points/sprint
Actual velocity	Completed points ÷ completed sprints	Calculate after sprint completion
Iteration-unit example	8.25 points ÷ 5 working days	1.65 planned points/day (illustrative only)

Planning assumption: each sprint is proposed as one week (five working days). Replace this duration and add actual dates when your team confirms the schedule.

4. Burndown Chart (Illustrative)

A burndown chart tracks remaining work over time. The chart below shows an idealized Sprint 1 example based on 11 planned story points over five working days. It is not actual project progress; update it using the remaining points recorded each day.

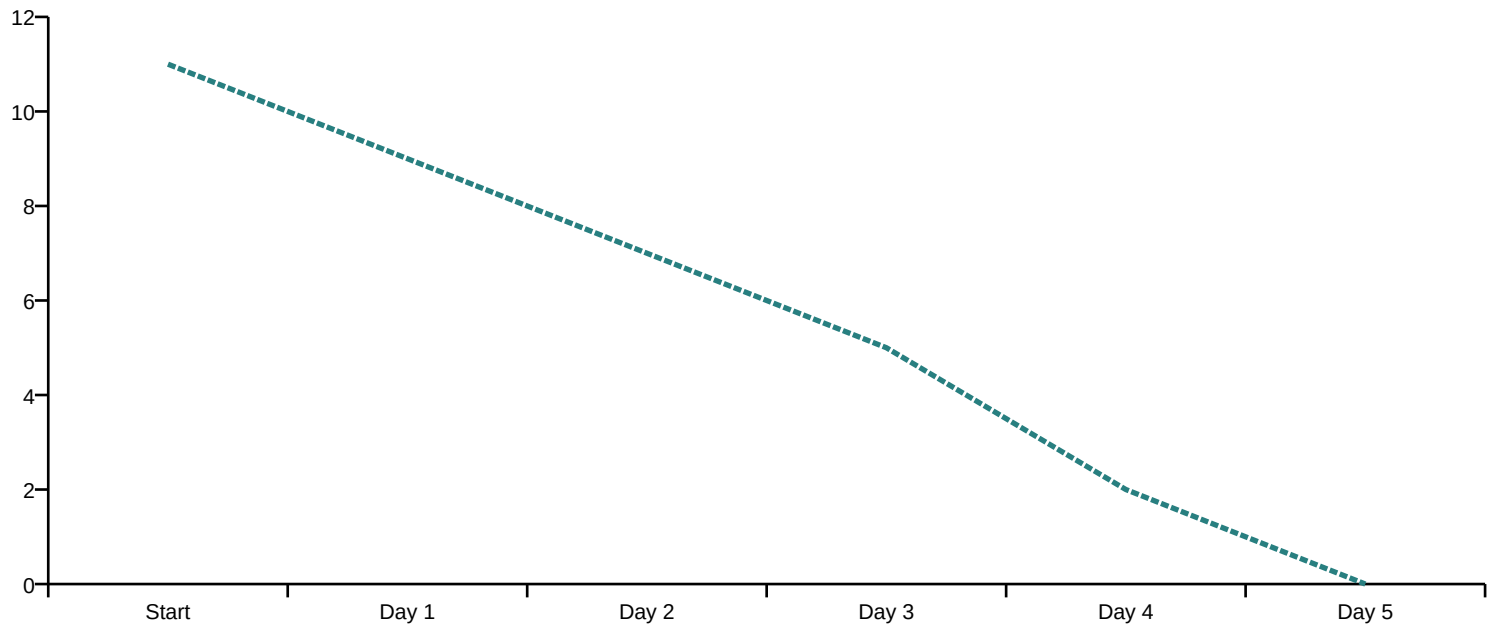

Timeline	Start	Day 1	Day 2	Day 3	Day 4	Day 5
Ideal remaining points	11	9	7	2	0	0
Actual remaining points	11	Update	Update	Update	Update	Update

5. Planning Assumptions

- The scope covers request submission, validation, record creation, manager approval, notifications, status tracking, IT review and testing.
- Dates and individual assignments remain open because the team calendar and member names were not supplied.
- Automatic inventory checks, procurement integration and delivery tracking are future enhancements, not assumed in the current scope.
